SNAPSERVE AI

Detailed 3-Year Budget, Sales Projection Production Capacity & Rs 5 Crore Round Plan

One CCPS seed round · four committed drawdowns
Rs 20 Cr pre-money · Rs 25 Cr post-money · 20% indicative dilution

Prepared for investor discussion · 14 August 2026
SnapServe AI Pvt Limited · Chennai

Executive summary

This document expands the investor pitch deck into a detailed operating budget. It translates each drawdown into hiring, product, production capacity, sales activity and measurable release milestones.

The recommendation is one legally committed Rs 5 crore CCPS round with four milestone-linked drawdowns—not four separate valuation rounds.

Metric	Base case	Investor interpretation
Current price / variable cost	Rs 5.00 / Rs 1.87 per minute	Rs 3.13 contribution; 62.6% variable margin
Initial drawdown	Rs 15 lakh	12-week bridge to reliability and first repeatable paying cohort
Full seed commitment	Rs 5 crore	18-month product, GTM and capacity plan
Y1 exit	10L monthly mins / Rs 50L MRR	250 paying accounts; Rs 6 Cr ARR run-rate
Y2 exit	50L monthly mins / Rs 2.5 Cr MRR	1,200 paying accounts; Rs 30 Cr ARR run-rate
Y3 exit	2 Cr monthly mins / Rs 10 Cr MRR	4,000 paying accounts; Rs 120 Cr ARR run-rate
Valuation	Rs 20 Cr pre / Rs 25 Cr post	20% seed ownership before new ESOP adjustment

Important: these are management targets, not guaranteed results. The model must be refreshed monthly using actual conversion, usage, collections and delivery cost.

1. Honest baseline and unit economics

The plan starts from live product usage, not a pre-product assumption. Baseline figures come from the SnapServe Admin view for the period available on 14 August 2026.

Metric	Value	Comment
Total users	417	Includes mixed/free/early users
Total calls	4,356	Live operating history
Total minutes	3,982	All-time baseline shown in Admin
Recognized usage (30d)	Rs 35,083	Current monthly revenue baseline
Wallet top-ups (30d)	Rs 31,100	Cash-in indicator
Current fixed opex	Rs 3L/month	Rs 1L Vobiz + Rs 2L rent/salaries/ops
Price / minute	Rs 5.00	Recognized platform revenue
Variable cost / minute	Rs 1.87	Telephony + AI delivery estimate
Contribution / minute	Rs 3.13	62.6% before fixed opex
Current fixed-cost break-even	~95,847 mins/month	Approximately Rs 4.79L monthly revenue

Why funding is required: the unit economics are positive, but current volume is only a small fraction of fixed-cost break-even. Capital primarily buys distribution, reliability, customer success and capacity.

2. Funding roadmap: one round, four drawdowns

All drawdowns should be committed in the same definitive financing documents. Objective release conditions and cure periods reduce the risk of later capital becoming discretionary.

Drawdown	Amount	Window	Release condition	Operating target
A — Initial close	Rs 15.00 L	Months 0-3	Signing and definitive CCPS documents	15 paying accounts · 30K mins/month · Rs 1.5L exit MRR
B — Foundation	Rs 85.00 L	Months 3-6	Reliability plan delivered and paying-customer pipeline validated	50 paying accounts · 1L mins/month · Rs 5L exit MRR
C — Early scale	Rs 1.50 Cr	Months 6-12	100 paying accounts and approximately 2L monthly minutes	250 paying accounts · path to 10L mins/month · Rs 50L exit MRR
D — Growth	Rs 2.50 Cr	Months 12-18	250 paying accounts and trajectory toward 10L monthly minutes	Repeatable GTM · positive monthly contribution · Series A readiness
Total	Rs 5.00 Cr	18 months	One CCPS financing	Series A-ready operating system

Founder answer: “We are raising one Rs 5 crore seed round through four committed CCPS drawdowns: Rs 15 lakh, Rs 85 lakh, Rs 1.5 crore and Rs 2.5 crore against agreed operating milestones.”

3. Tranche A — Initial close

Capital: Rs 15.00 L **Deployment:** Months 0-3 **Release:** Signing and definitive CCPS documents

15 paying accounts · 30K mins/month · Rs 1.5L exit MRR

Budget allocation

Budget category	Amount	%	What it funds
Engineering & product	Rs 3.00 L	20.0%	Reliability fixes, analytics, Meet/WhatsApp completion, QA
Sales & customer success	Rs 2.00 L	13.3%	Founder-led demos, POCs, onboarding, CRM/outreach
Production & infrastructure	Rs 3.00 L	20.0%	Three months Vobiz commitment, cloud and observability
Marketing	Rs 1.00 L	6.7%	Case studies, demo assets, website and targeted outreach
Legal, payroll & operations	Rs 6.00 L	40.0%	Core payroll/rent, CCPS/legal work and contingency
Total	Rs 15.00 L	100.0%	Must reconcile to bank drawdown and board-approved budget

First Rs 15 lakh: 12-week execution budget

Month	Opening focus	Budget guardrail	Target evidence
Month 1	Fix reliability, complete financing/legal, protect current customers	Up to Rs 5L	Uptime dashboard, signed docs, active pipeline
Month 2	POCs, onboarding, case-study calls and production monitoring	Up to Rs 5L	5-8 paying accounts, measured usage
Month 3	Repeatable sales motion and Tranche B readiness	Up to Rs 5L	15 paying, 30K mins/month, Rs 1.5L MRR

Do not use the Rs 15 lakh for broad hiring. It is a controlled bridge: protect delivery, prove repeatable paid usage and unlock the committed Rs 85 lakh foundation drawdown.

4. Tranche B — Foundation

Capital: Rs 85.00 L **Deployment:** Months 3-6 **Release:** Reliability plan delivered and paying-customer pipeline validated

50 paying accounts · 1L mins/month · Rs 5L exit MRR

Budget allocation

Budget category	Amount	%	What it funds
Engineering & product	Rs 35.00 L	41.2%	Core hires, uptime, security, campaign and analytics quality
Sales & customer success	Rs 20.00 L	23.5%	First GTM hires, vertical demos, onboarding playbook
Production & infrastructure	Rs 13.00 L	15.3%	Telephony capacity, inference, cloud and monitoring
Marketing	Rs 7.00 L	8.2%	Vertical content, founder events, lead generation
Legal, payroll & operations	Rs 10.00 L	11.8%	Operations, compliance, finance controls and reserve
Total	Rs 85.00 L	100.0%	Must reconcile to bank drawdown and board-approved budget

Release-control rule

Management reports monthly actual-versus-budget by category. Any category variance above 15% requires a written reforecast; unused funds remain in runway reserve rather than being automatically spent.

5. Tranche C — Early scale

Capital: Rs 1.50 Cr **Deployment:** Months 6-12 **Release:** 100 paying accounts and approximately 2L monthly minutes

250 paying accounts · path to 10L mins/month · Rs 50L exit MRR

Budget allocation

Budget category	Amount	%	What it funds
Engineering & product	Rs 62.00 L	41.3%	Scale, Indic quality, partner controls, reporting and automation
Sales & customer success	Rs 45.00 L	30.0%	Vertical AEs, onboarding team and partner activation
Production & infrastructure	Rs 22.00 L	14.7%	Capacity reserves, routing, monitoring and support
Marketing	Rs 15.00 L	10.0%	Case studies, demand generation, events and channel enablement
Legal, payroll & operations	Rs 6.00 L	4.0%	Hiring, contracts, compliance and operating reserve
Total	Rs 1.50 Cr	100.0%	Must reconcile to bank drawdown and board-approved budget

Release-control rule

Management reports monthly actual-versus-budget by category. Any category variance above 15% requires a written reforecast; unused funds remain in runway reserve rather than being automatically spent.

6. Tranche D — Growth

Capital: Rs 2.50 Cr **Deployment:** Months 12-18 **Release:** 250 paying accounts and trajectory toward 10L monthly minutes

Repeatable GTM · positive monthly contribution · Series A readiness

Budget allocation

Budget category	Amount	%	What it funds
Engineering & product	Rs 1.00 Cr	40.0%	Enterprise reliability, platform breadth, security and scale
Sales & customer success	Rs 83.00 L	33.2%	National GTM, partner success and enterprise onboarding
Production & infrastructure	Rs 37.00 L	14.8%	Volume capacity, working capital and resilience
Marketing	Rs 27.00 L	10.8%	Category building, events, content and pipeline acceleration
Legal, payroll & operations	Rs 3.00 L	1.2%	Governance, diligence readiness and controls
Total	Rs 2.50 Cr	100.0%	Must reconcile to bank drawdown and board-approved budget

Release-control rule

Management reports monthly actual-versus-budget by category. Any category variance above 15% requires a written reforecast; unused funds remain in runway reserve rather than being automatically spent.

7. Consolidated Rs 5 crore use of funds

The drawdown budgets reconcile exactly to the use-of-funds percentages shown in the pitch deck.

Category	A	B	C	D	Total	% of round
Engineering & product	Rs 3.00 L	Rs 35.00 L	Rs 62.00 L	Rs 1.00 Cr	Rs 2.00 Cr	40.0%
Sales & customer success	Rs 2.00 L	Rs 20.00 L	Rs 45.00 L	Rs 83.00 L	Rs 1.50 Cr	30.0%
Production & infrastructure	Rs 3.00 L	Rs 13.00 L	Rs 22.00 L	Rs 37.00 L	Rs 75.00 L	15.0%
Marketing	Rs 1.00 L	Rs 7.00 L	Rs 15.00 L	Rs 27.00 L	Rs 50.00 L	10.0%
Legal, payroll & operations	Rs 6.00 L	Rs 10.00 L	Rs 6.00 L	Rs 3.00 L	Rs 25.00 L	5.0%
Total	Rs 15L	Rs 85L	Rs 1.50Cr	Rs 2.50Cr	Rs 5.00Cr	100.0%

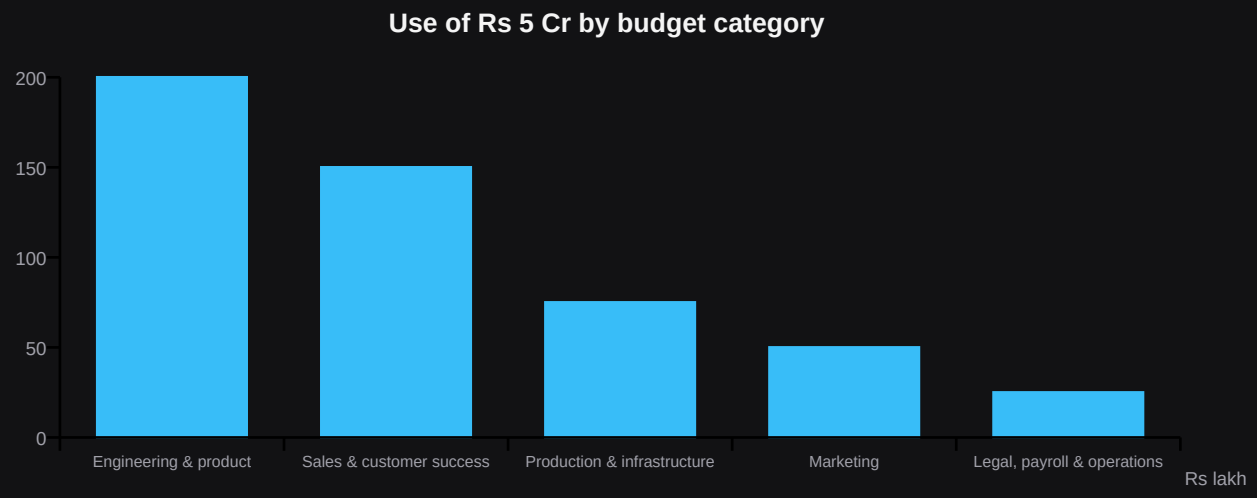

8. Quarterly sales and revenue projection

Revenue is usage-based: quarterly minutes × Rs 5 per minute. Account targets imply approximately 4,000-5,000 monthly minutes per mature paying account.

Quarter	Avg mins/mo	Accounts at exit	Revenue	Exit direction
Y1 Q1	0.20 L	15	Rs 0.03 Cr	Prove paid cohort
Y1 Q2	1.00 L	50	Rs 0.15 Cr	Vertical repeatability
Y1 Q3	3.00 L	120	Rs 0.45 Cr	Vertical repeatability
Y1 Q4	7.80 L	250	Rs 1.17 Cr	Seed milestone
Y2 Q1	15.00 L	400	Rs 2.25 Cr	Scale accounts + partners
Y2 Q2	22.00 L	650	Rs 3.30 Cr	Scale accounts + partners
Y2 Q3	28.00 L	900	Rs 4.20 Cr	Scale accounts + partners
Y2 Q4	35.00 L	1,200	Rs 5.25 Cr	Scale accounts + partners
Y3 Q1	60.00 L	1,800	Rs 9.00 Cr	Scale accounts + partners
Y3 Q2	90.00 L	2,500	Rs 13.50 Cr	Scale accounts + partners
Y3 Q3	130.00 L	3,200	Rs 19.50 Cr	Scale accounts + partners
Y3 Q4	160.00 L	4,000	Rs 24.00 Cr	Scale accounts + partners

9. Sales budget and funnel assumptions

The sales plan should be managed as a funnel. These starting assumptions must be replaced with actual CRM conversion data after the first 90 days.

Stage	Initial assumption	Y1 operating requirement	Owner
Qualified opportunities	20% of targeted prospects	Build vertical lists and partner referrals	Founder / SDR
POC / live demo	35% of qualified opportunities	Demo using customer workflow and phone number	Founder / Solutions
Paid activation	30% of POCs	Wallet funded and first 1,000 minutes	AE / Onboarding
90-day retained account	70% of paid activations	Usage review, KB quality, campaign support	Customer Success
Expansion	25% of retained accounts / quarter	More agents, campaigns, numbers or partner clients	CS / AE

Sales and customer-success capital

Period	Sales & CS capital	Primary spending	Output target
Tranche A	Rs 2L	Founder demos, POCs, onboarding	15 paying accounts
Tranche B	Rs 20L	First GTM hires and repeatable vertical motion	50 paying accounts
Tranche C	Rs 45L	AEs, onboarding and partner activation	250 paying accounts
Tranche D	Rs 83L	National GTM and enterprise customer success	Series A-ready pipeline
Total	Rs 1.50Cr	30% of the seed round	4,000 paying accounts by Y3 exit

Governance KPI: track CAC separately for direct SMB, enterprise and partner channels. Do not publish LTV:CAC until retention and expansion cohorts are mature.

10. Production and service-delivery budget

For SnapServe, “production” means the cost and capacity required to deliver completed AI voice minutes: telephony, STT/TTS, LLM inference, cloud, monitoring, QA and support.

Quarter	Quarter mins	Revenue	Variable delivery cost	Gross contribution	Var. margin
Y1 Q1	0.60 L	Rs 0.03 Cr	Rs 0.01 Cr	Rs 0.02 Cr	62.6%
Y1 Q2	3.00 L	Rs 0.15 Cr	Rs 0.06 Cr	Rs 0.09 Cr	62.6%
Y1 Q3	9.00 L	Rs 0.45 Cr	Rs 0.17 Cr	Rs 0.28 Cr	62.6%
Y1 Q4	23.40 L	Rs 1.17 Cr	Rs 0.44 Cr	Rs 0.73 Cr	62.6%
Y2 Q1	45.00 L	Rs 2.25 Cr	Rs 0.79 Cr	Rs 1.46 Cr	65.0%
Y2 Q2	66.00 L	Rs 3.30 Cr	Rs 1.16 Cr	Rs 2.14 Cr	65.0%
Y2 Q3	84.00 L	Rs 4.20 Cr	Rs 1.47 Cr	Rs 2.73 Cr	65.0%
Y2 Q4	105.00 L	Rs 5.25 Cr	Rs 1.84 Cr	Rs 3.41 Cr	65.0%
Y3 Q1	180.00 L	Rs 9.00 Cr	Rs 2.88 Cr	Rs 6.12 Cr	68.0%
Y3 Q2	270.00 L	Rs 13.50 Cr	Rs 4.32 Cr	Rs 9.18 Cr	68.0%
Y3 Q3	390.00 L	Rs 19.50 Cr	Rs 6.24 Cr	Rs 13.26 Cr	68.0%
Y3 Q4	480.00 L	Rs 24.00 Cr	Rs 7.68 Cr	Rs 16.32 Cr	68.0%

Production controls

Control	Target	Why it matters
Blended variable cost	≤ Rs 1.87/min Y1; Rs 1.60/min by Y3	Protects contribution margin
Capacity headroom	≥ 30% above rolling 30-day peak	Prevents campaign congestion
Platform availability	≥ 99.5% in Tranche A; ≥ 99.9% at enterprise scale	Supports customer trust
Call completion	Improve from current 54% with routing and retries	Directly drives billable value
Cost reconciliation	Daily provider usage vs wallet ledger	Prevents margin leakage
Quality review	Sample calls by language, vertical and provider	Maintains conversion quality

11. Three-year profit and loss projection

Annual revenue uses average monthly volume; ARR uses the exit run-rate. Mixing these two is a common forecasting error.

Rs crore	Year 1	Year 2	Year 3
Recognized revenue	Rs 1.80 Cr	Rs 15.00 Cr	Rs 66.00 Cr
Variable delivery cost	Rs -0.67 Cr	Rs -5.25 Cr	Rs -21.12 Cr
Gross contribution	Rs 1.13 Cr	Rs 9.75 Cr	Rs 44.88 Cr
Operating expenses	Rs -2.40 Cr	Rs -8.00 Cr	Rs -24.00 Cr
EBITDA	Rs -1.27 Cr	Rs 1.75 Cr	Rs 20.88 Cr
EBITDA margin	-70.7%	11.7%	31.6%
Exit ARR run-rate	Rs 6 Cr	Rs 30 Cr	Rs 120 Cr

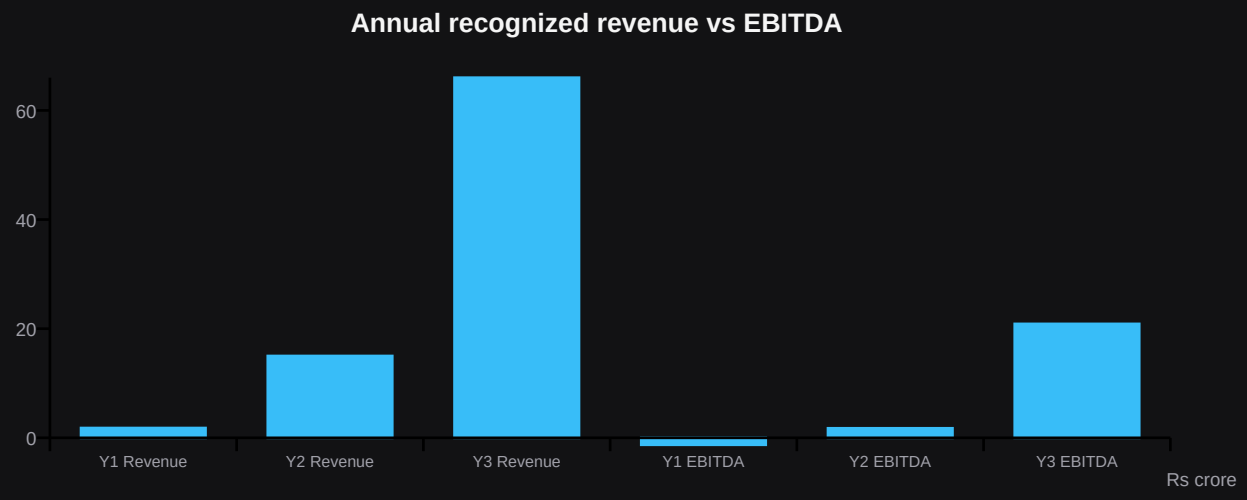

Base-case interpretation: Year 1 is investment-heavy, Year 2 establishes operating leverage, and Year 3 scales margin. The Year 3 result requires the partner channel and enterprise retention assumptions to hold.

12. Quarterly operating budget and cash discipline

EBITDA below excludes financing flows and working-capital timing. Tranche receipts are balance-sheet financing, not revenue.

Quarter	Gross contribution	Operating expenses	EBITDA	Management action
Y1 Q1	Rs 0.02 Cr	Rs 0.35 Cr	Rs -0.33 Cr	Protect runway / prove usage
Y1 Q2	Rs 0.09 Cr	Rs 0.50 Cr	Rs -0.41 Cr	Protect runway / prove usage
Y1 Q3	Rs 0.28 Cr	Rs 0.65 Cr	Rs -0.37 Cr	Protect runway / prove usage
Y1 Q4	Rs 0.73 Cr	Rs 0.90 Cr	Rs -0.17 Cr	Protect runway / prove usage
Y2 Q1	Rs 1.46 Cr	Rs 1.50 Cr	Rs -0.04 Cr	Monitor collections
Y2 Q2	Rs 2.14 Cr	Rs 1.80 Cr	Rs 0.34 Cr	Reinvest within approved budget
Y2 Q3	Rs 2.73 Cr	Rs 2.20 Cr	Rs 0.53 Cr	Reinvest within approved budget
Y2 Q4	Rs 3.41 Cr	Rs 2.50 Cr	Rs 0.91 Cr	Reinvest within approved budget
Y3 Q1	Rs 6.12 Cr	Rs 4.50 Cr	Rs 1.62 Cr	Reinvest within approved budget
Y3 Q2	Rs 9.18 Cr	Rs 5.50 Cr	Rs 3.68 Cr	Reinvest within approved budget
Y3 Q3	Rs 13.26 Cr	Rs 6.50 Cr	Rs 6.76 Cr	Reinvest within approved budget
Y3 Q4	Rs 16.32 Cr	Rs 7.50 Cr	Rs 8.82 Cr	Reinvest within approved budget

Cash controls

Control	Rule
Minimum runway	Maintain at least 9 months of board-approved base operating expense after each drawdown.
Hiring gates	No role opens without 12-month loaded cost, owner, KPI and approved start date.
Receivables	Enterprise credit terms require approval; wallet-funded SMB usage remains prepaid.
Provider commitments	Capacity contracts must stay below conservative volume case unless cancellable.
Reforecast	Refresh rolling 18-month cash forecast monthly; board review quarterly.

13. Hiring and operating-expense plan

Team growth is a ceiling, not an automatic hiring target. Hiring follows revenue, reliability and sales productivity evidence.

Function	End Y1	End Y2	End Y3	Primary KPI
Founders / leadership	2	4	6	Capital allocation and milestone delivery
Engineering / AI / product	5	14	30	Reliability, quality and release velocity
Sales / partnerships	2	8	20	Pipeline, conversion and payback
Customer success / solutions	2	6	14	Activation, retention and expansion
Operations / finance / people	1	3	6	Controls, hiring and collections
Support / QA	0-1 shared	4	4	Resolution time and sampled-call quality
Total target	12	35	80	Subject to approved hiring gates

Operating-expense envelope

Opex view	Year 1	Year 2	Year 3
Annual operating expenses	Rs 2.40 Cr	Rs 8.00 Cr	Rs 24.00 Cr
Average monthly opex	Rs 20L	Rs 66.7L	Rs 2.00 Cr
End-of-year team	12	35	80
Primary scaling driver	Product + first GTM	National GTM + CS	Enterprise + platform scale

14. Scenario and sensitivity analysis

The largest valuation-sensitive variable is usage growth. The first 90 days should establish whether the base case is credible.

Case	Y1 exit mins/month	Y1 exit MRR	Y1 exit ARR	Required response
Conservative	5L	Rs 25L	Rs 3 Cr	Slow hiring; prioritize retention and partner conversion
Base	10L	Rs 50L	Rs 6 Cr	Execute approved tranche and hiring plan
Aggressive	20L	Rs 1 Cr	Rs 12 Cr	Add capacity only after collections and quality hold

Downside controls

Risk	Early warning	Mitigation
Sales conversion below plan	POC-to-paid <20%	Narrow vertical, strengthen proof and founder-led discovery
Usage per account below plan	<2,500 mins/account/month	Move toward campaign-heavy and partner accounts
Variable cost rises	>Rs 2/min for two months	Route providers, renegotiate volume and tighten features
Later tranche delayed	<6 months runway	Freeze hiring and activate minimum viable Rs 1 Cr plan
Collections slow	DSO >45 days	Prepaid wallet, credit limits and enterprise approval
Quality or uptime drops	Completion/availability misses SLA	Pause acquisition, fix reliability and add capacity

15. Investor terms and diligence readiness

Indicative commercial position: Rs 20 crore pre-money, Rs 25 crore post-money, Rs 5 crore CCPS and 20% seed ownership before any new ESOP pool adjustment.

Issue	Founder position to discuss	Why it matters
Instrument	CCPS; final conversion and rights drafted by counsel	Standard priced seed structure for an Indian Pvt Ltd
Drawdowns	Entire Rs 5 Cr committed at signing	Avoids financing risk after hiring begins
Milestones	Objective, measurable and with cure periods	Prevents subjective withholding
Valuation	Fixed across all four drawdowns	Avoids hidden repricing
Liquidation preference	Target 1x non-participating	Avoids double-dip economics
Anti-dilution	Broad-based weighted average; no full ratchet	Protects founders in future financing
ESOP	Model pool expansion explicitly	Pre-money pools increase founder dilution
Board / reserved matters	Proportionate, clearly scoped	Preserves operating ability
Legal review	Indian startup counsel + CA/CS	CCPS, FEMA and company-law compliance

This document is a management planning model, not legal, tax or investment advice. Definitive documents control.

16. Monthly board dashboard

Every monthly investor update should compare actual results with the approved budget and explain corrective action.

Section	Metrics to report	Decision enabled
Sales	Qualified pipeline, demos, POCs, paid activations, CAC	Whether to add GTM capacity
Revenue	Wallet cash-in, recognized usage, MRR, expansion, collections	Quality and durability of growth
Usage	Minutes, calls, completion, minutes/account, channel mix	Capacity and customer value
Production	Cost/min, provider mix, uptime, latency, failure rate	Margin and reliability action
Customer	Activation, 30/90-day retention, support, NPS/case studies	Retention and expansion priorities
Cash	Opening cash, burn, runway, budget variance, receivables	Hiring and tranche timing
People	Headcount, loaded cost, open roles, productivity	Hiring gate decisions
Milestones	Tranche release evidence and next constraints	Board/investor alignment

Next operating step

At the end of each month, replace forecast values with actuals, roll the model forward by one month, and update conservative/base/aggressive cases. Investor confidence comes from forecast accuracy and transparent corrections—not only from ambitious targets.
